
EZ **EZ MANAGE** DELIVERY ETA

EzManage ETA — 5 phases, ~10 weeks

The current sprint laid out week by week. Each phase ends in a **manager demo** (M1–M5), with a short progress check every week in between. Durations are indicative — they move with team size.

PHASES	TIMELINE	MILESTONES	REVIEWS
5	**~10** weeks	**5** M1–M5	**Weekly** + demos

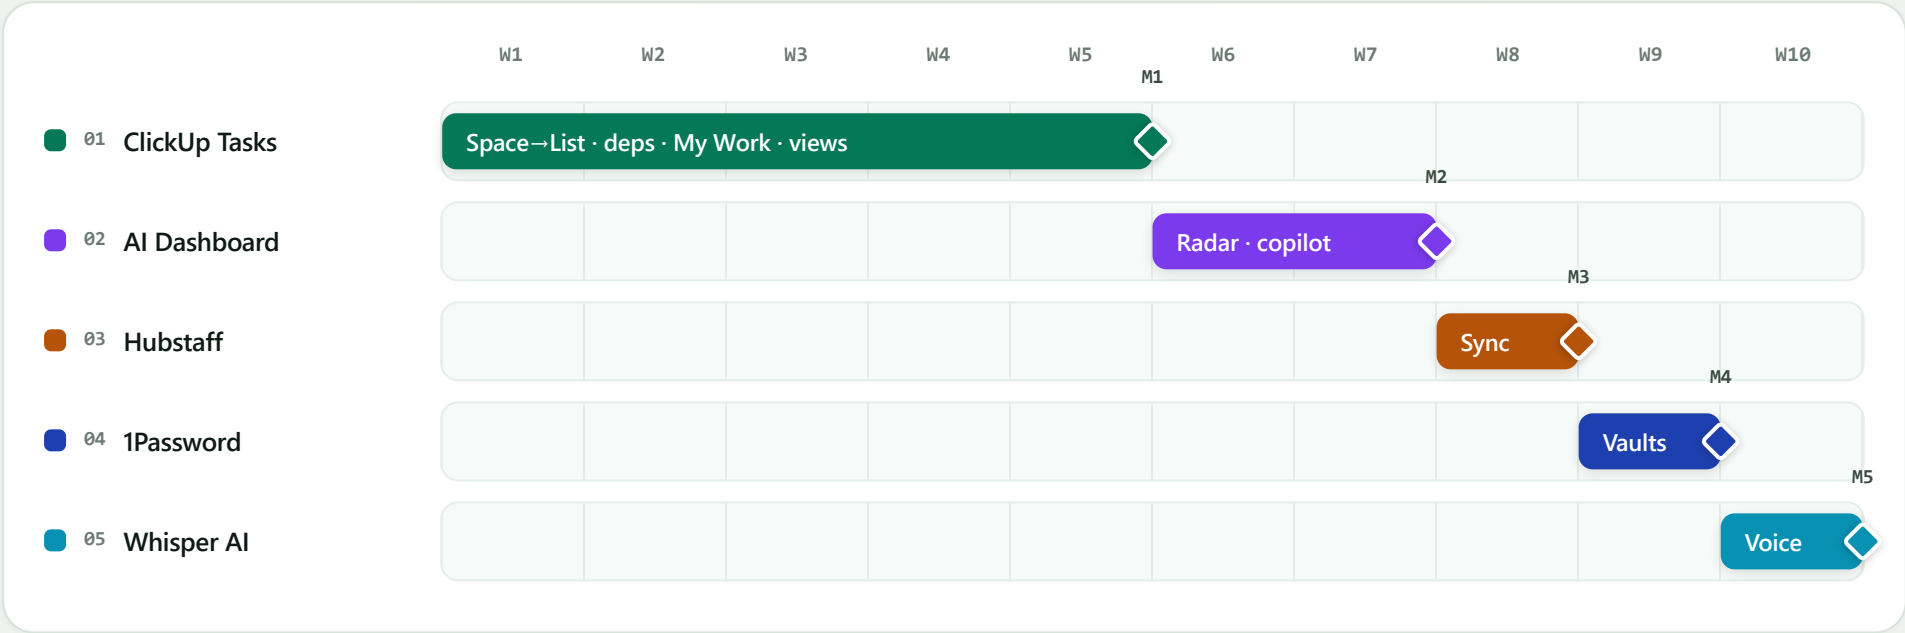

◆ Diamond = milestone demo (M1–M5) ● Manager review Bars span the weeks each phase runs.

W1

Space → Folder → List hierarchy + List view

ClickUp structure on top of the existing boards.

REVIEW #1

W2

Dependencies · priorities · checklists/subtasks · multiple assignees

The task-depth ClickUp is known for.

REVIEW #2

W3

My Work inbox · Goals/OKRs · custom statuses · tags

Personal view + per-list workflows.

REVIEW #3

W4–5

Timeline/Workload views · time tracking · automations · docs

Rounds out ClickUp parity.

M1 — CLICKUP DEMO

W6

Attention radar + live pulse

CEO sees what needs action, live.

REVIEW #4

W7

AI copilot + drill-down tiles

Ask questions over live data.

M2 — AI DASHBOARD DEMO

W8

Hubstaff — connect + sync time, activity, screenshots

Real tracked time on tasks + dashboard.

M3 — HUBSTAFF DEMO

W9

1Password — vaults, role access, audit

Secure client credentials, no chat sharing.

M4 — 1PASSWORD DEMO

W10

Whisper — voice notes + transcription

Voice notes become searchable text.

M5 — WHISPER DEMO

Manager meeting cadence

Weekly — a short progress check at each week's end. **Milestone demos (M1–M5)** — show the working feature. **Next meeting:** end of W1 — the ClickUp hierarchy (Space → List).
